


Development at Bretonside - Plymouth

Project Progress Site Number (M1432)

Works progressed this week include:

- Structural steelwork installation to Zone 2 commenced.
- Preparation works to Zone 3 ready for steelwork installation.
- Drainage and concrete slab preparation within the viaduct undercroft ongoing.
- Bases completed to Zone 5 ready for steelwork installation next week.

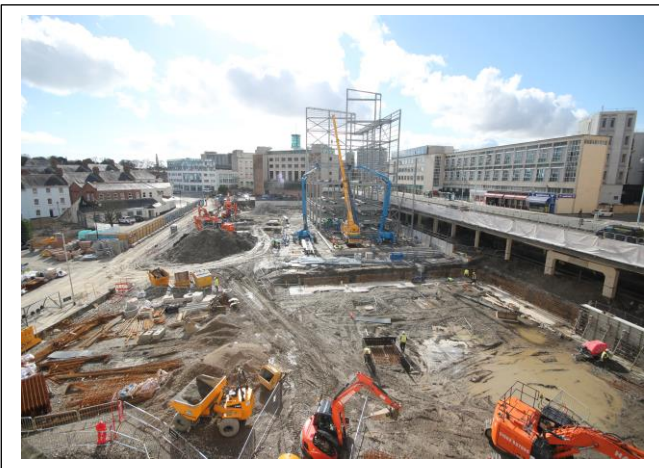

View from Gala Bingo



View from Primark



Steelwork installation commenced to Zone 2.




Prep work to Zone 5 ready for steel erection next week.

Project Progress

Drake Circus Development



Concrete pours ongoing to RBS retaining wall

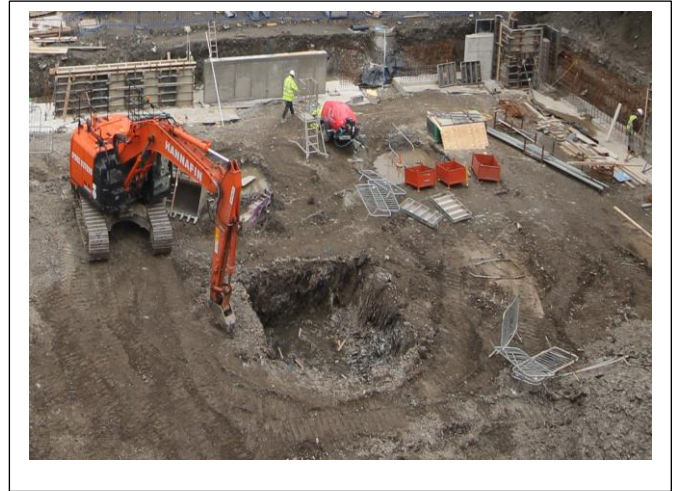

Bases to Zone 3 commenced, prep work to retaining walls ongoing.



Prep work to undercroft completed ready for render repairs and decoration.



Drainage installation to undercroft ongoing.

Works programmed for the next week include:

- Commence installation of structural steelwork to Zone 5.
- Continue with drainage to undercroft and preparation for slab pours.
- Continue with forming bases to Zone 3 ready for steelwork installation.
- Meeting arranged with CTP on Tuesday 10th April to discuss work placement for ex-forces personnel.

Contact details:

Name: Stuart Goss
Job Title: Project Director
E: Stuart.goss@mclarengroup.com
M: 07460568086

Name: Frank Edge
Job Title: Senior Site Manager
E: Frank.Edge@McLarengroup.com
M: 07739 881595
