


## Development at Bretonside - Plymouth


### Project Progress Site Number (M1432)

Works progressed this week include:

- Structural steelwork installation to Zone 5 ongoing.
- Lane closure on Exeter Street viaduct commenced.
- Intumescent painting of structural steelwork commenced ready for external cladding.
- Site visit held with engineering and site management students from Plymouth University.

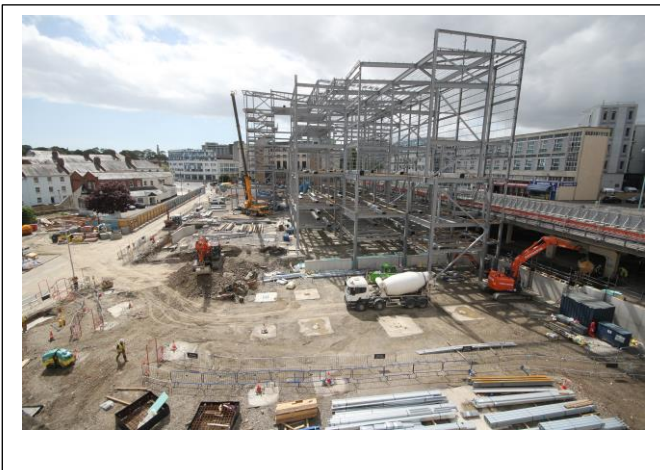

View from Gala Bingo

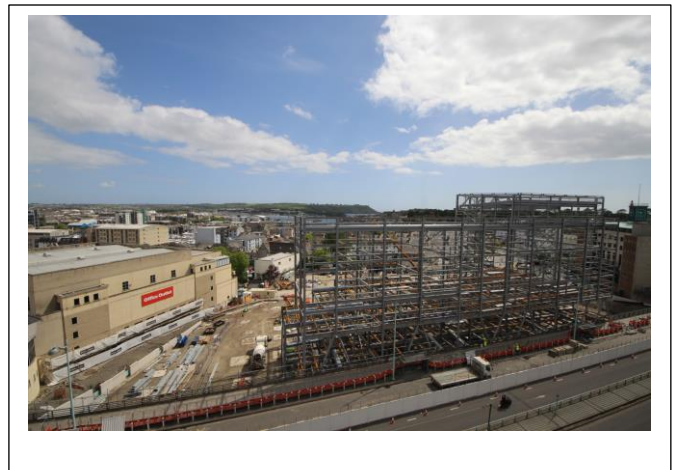

View from Primark



Steelwork installation ongoing to Zone 5.



Exeter street lane closure commenced.

# Project Progress


## Drake Circus Development




Site visit with engineering students from Plymouth University.



Intumescent painting commenced to structural steelwork

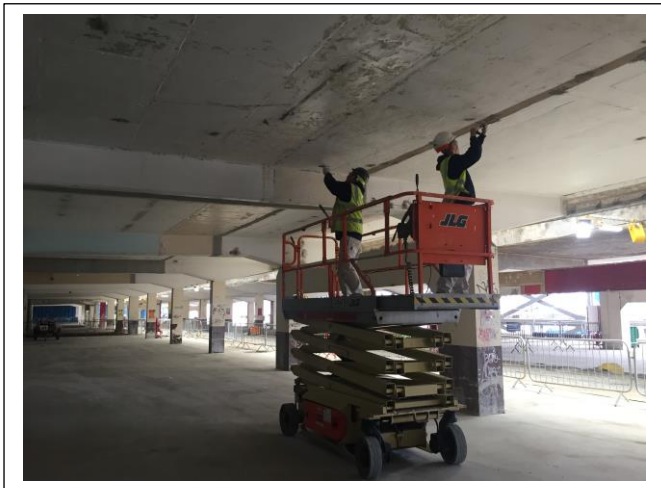

Preparation for decoration to undercroft ongoing

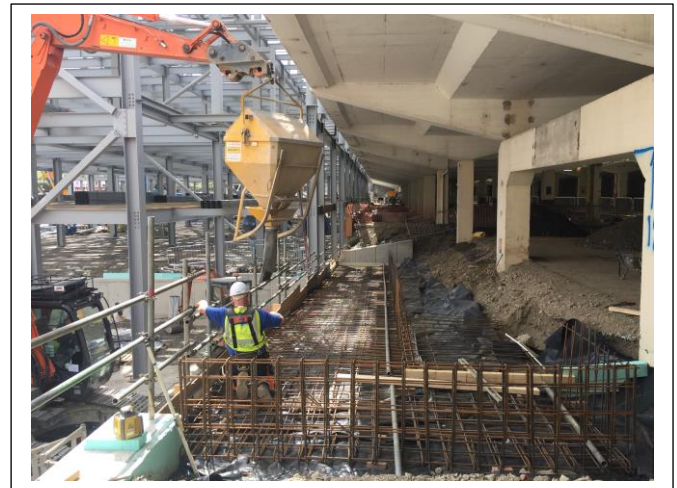

Concrete pour of pedestrian access ramp to undercroft car park.

Works programmed for the next week include:

- Continue with installation of structural steelwork to Zone 5.
- Continue with intumescent painting to structural steelwork and decoration to undercroft.
- Commence external cladding works.
- Site visit on Thursday 17<sup>th</sup> May arranged with students from Mount Tamar Secondary School.

Contact details:

Name: Stuart Goss  
Job Title: Project Director  
E: [Stuart.goss@mclarengroup.com](mailto:Stuart.goss@mclarengroup.com)  
M: 07460568086

Name: Frank Edge  
Job Title: Senior Site Manager  
E: [Frank.Edge@McLarengroup.com](mailto:Frank.Edge@McLarengroup.com)  
M: 07739 881595
